M. C. F. C. D.

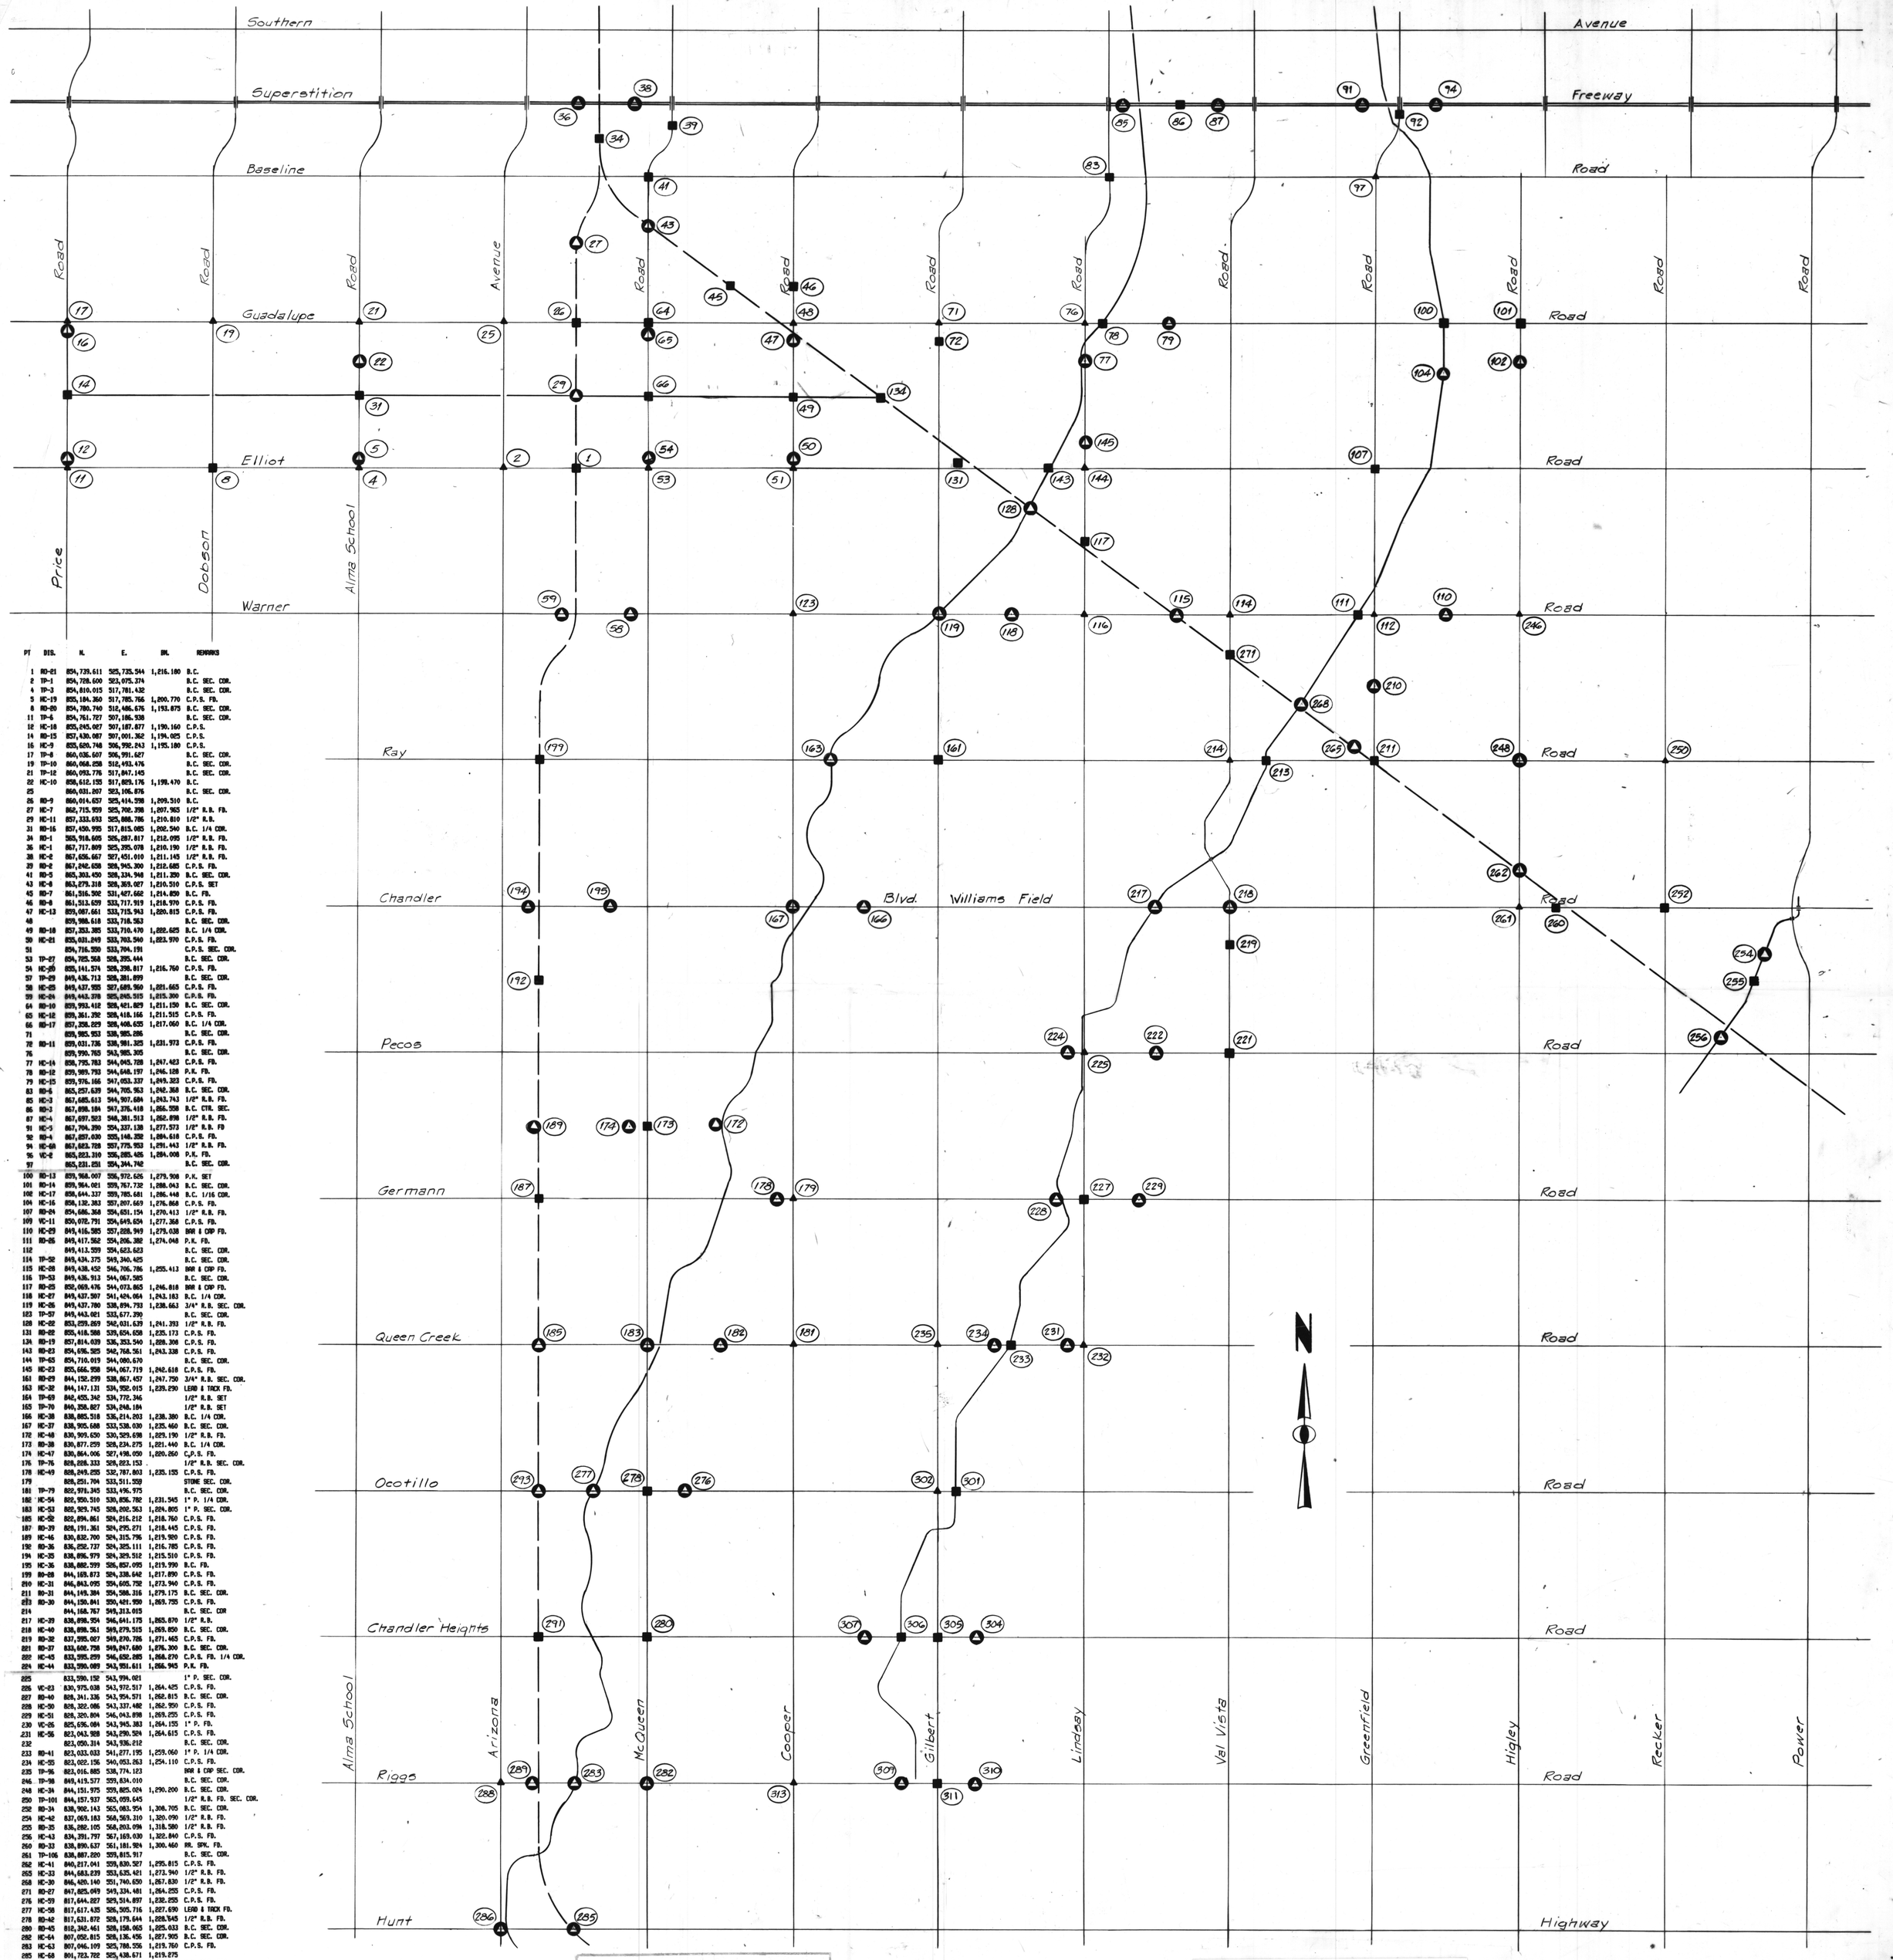

PT	DIS.	N.	E.	EL.	REMARKS
1	RD-21	854,739.611	525,735.544	1,216.180	B.C.
2	TP-1	854,728.600	523,075.374		B.C. SEC. COR.
4	TP-3	854,810.015	517,781.432		B.C. SEC. COR.
5	HC-19	855,184.360	517,785.766	1,200.770	C.P.S. FD.
8	RD-20	854,780.740	512,486.676	1,193.875	B.C. SEC. COR.
11	TP-6	854,761.727	507,186.938		B.C. SEC. COR.
12	HC-16	855,245.027	507,187.877	1,190.160	C.P.S.
14	RD-15	857,430.087	507,001.362	1,194.025	C.P.S.
16	HC-9	855,620.748	506,992.243	1,195.180	C.P.S.
17	TP-8	860,035.607	506,991.627		B.C. SEC. COR.
19	TP-10	860,068.258	512,493.476		B.C. SEC. COR.
21	TP-12	860,093.776	517,847.145		B.C. SEC. COR.
22	HC-10	858,612.155	517,829.176	1,198.470	B.C.
25		860,031.207	523,106.876		B.C. SEC. COR.
26	RD-9	860,014.657	525,414.298	1,209.510	B.C.
27	HC-7	862,715.959	525,702.398	1,207.965	1/2" R.B. FD.
29	HC-11	857,333.693	525,888.786	1,210.810	1/2" R.B.
31	RD-16	857,450.995	517,815.085	1,202.540	B.C. 1/4 COR.
34	RD-1	865,918.605	526,287.817	1,212.095	1/2" R.B. FD.
36	HC-1	867,717.609	525,395.078	1,210.190	1/2" R.B. FD.
38	HC-2	867,656.667	527,451.010	1,211.145	1/2" R.B. FD.
39	RD-2	867,242.658	528,945.200	1,212.685	C.P.S. FD.
41	RD-5	865,303.450	528,334.948	1,211.250	B.C. SEC. COR.
43	HC-6	863,275.218	528,359.027	1,210.510	C.P.S. SET
45	RD-7	861,516.502	531,427.662	1,214.859	B.C. FD.
46	RD-8	861,513.659	533,717.919	1,218.970	C.P.S. FD.
47	HC-13	859,087.661	533,715.943	1,220.815	C.P.S. FD.
48		859,988.618	533,718.353		B.C. SEC. COR.
49	RD-18	857,253.385	533,710.470	1,222.625	B.C. 1/4 COR.
50	HC-21	855,031.249	533,703.590	1,223.970	C.P.S. FD.
51		854,716.350	533,704.191		C.P.S. SEC. COR.
53	TP-27	854,725.568	528,395.444		B.C. SEC. COR.
54	HC-20	855,141.574	528,398.817	1,216.760	C.P.S. FD.
57	TP-29	849,435.713	528,381.899		B.C. SEC. COR.
58	HC-25	849,437.935	527,689.960	1,221.665	C.P.S. FD.
59	HC-24	849,443.378	525,265.515	1,215.300	C.P.S. FD.
64	RD-10	859,953.412	528,421.829	1,211.150	B.C. SEC. COR.
65	HC-12	859,361.392	528,418.166	1,211.515	C.P.S. FD.
66	RD-17	857,358.829	528,408.635	1,217.060	B.C. 1/4 COR.
71		859,985.953	538,985.286		B.C. SEC. COR.
72	RD-11	859,031.736	538,981.325	1,231.973	C.P.S. FD.
76		859,990.765	543,985.305		B.C. SEC. COR.
77	HC-14	858,755.783	544,045.728	1,247.483	C.P.S. FD.
78	RD-12	859,989.793	544,648.157	1,246.128	P.K. FD.
79	HC-15	859,976.166	547,653.337	1,249.323	C.P.S. FD.
83	RD-6	865,257.639	544,705.963	1,242.368	B.C. SEC. COR.
85	HC-3	867,685.613	544,907.684	1,243.743	1/2" R.B. FD.
86	RD-3	867,698.184	547,376.418	1,266.558	B.C. CTR. SEC.
87	HC-4	867,697.523	548,381.513	1,262.898	1/2" R.B. FD.
91	HC-5	867,704.390	554,337.138	1,277.573	1/2" R.B. FD
92	RD-4	867,887.630	555,148.252	1,284.618	C.P.S. FD.
94	HC-60	867,883.728	557,775.953	1,291.443	1/2" R.B. FD.
96	VC-2	865,823.310	536,885.405	1,284.008	P.K. FD.
97		865,231.251	554,344.742		B.C. SEC. COR.
100	RD-13	859,968.007	556,972.626	1,279.908	P.K. SET
101	RD-14	859,964.021	559,767.732	1,288.043	B.C. SEC. COR.
102	HC-17	858,644.337	559,785.681	1,286.448	B.C. 1/16 COR.
104	HC-16	856,132.383	557,897.669	1,276.868	C.P.S. FD.
107	RD-24	854,686.368	554,651.154	1,270.413	1/2" R.B. FD.
109	VC-11	850,072.791	554,649.654	1,277.368	C.P.S. FD.
110	HC-29	849,416.585	557,228.949	1,273.038	BAR & CAP FD.
111	RD-25	849,417.562	554,206.382	1,274.048	P.K. FD.
112		849,413.559	554,623.623		B.C. SEC. COR.
114	TP-52	849,434.375	549,340.425		B.C. SEC. COR.
115	HC-28	849,438.452	546,706.786	1,255.413	BAR & CAP FD.
116	TP-53	849,436.913	544,067.585		B.C. SEC. COR.
117	RD-26	852,669.476	544,073.865	1,246.818	BAR & CAP FD.
118	HC-27	849,437.597	541,424.064	1,243.183	B.C. 1/4 COR.
119	HC-26	849,437.780	538,894.793	1,238.663	3/4" R.B. SEC. COR.
123	TP-57	849,443.021	533,677.390		B.C. SEC. COR.
128	HC-22	853,259.269	542,031.639	1,241.393	1/2" R.B. FD.
131	RD-22	855,418.588	539,654.658	1,235.173	C.P.S. FD.
134	RD-19	857,814.039	536,353.540	1,228.308	C.P.S. FD.
143	RD-23	854,696.325	540,768.561	1,243.338	C.P.S. FD.
144	TP-65	854,710.019	544,080.670		B.C. SEC. COR.
145	HC-23	855,666.958	544,067.719	1,262.618	C.P.S. FD.
161	RD-29	844,152.299	538,867.457	1,247.750	3/4" R.B. SEC. COR.
163	HC-32	844,147.131	534,952.015	1,239.290	LEAD & TACK FD.
164	TP-69	842,455.342	534,772.346		1/2" R.B. SET
165	TP-70	840,358.827	534,248.184		1/2" R.B. SET
166	HC-38	838,885.518	536,214.803	1,238.380	B.C. 1/4 COR.
167	HC-37	838,905.608	533,538.030	1,235.460	B.C. SEC. COR.
172	HC-48	830,909.650	530,529.698	1,229.190	1/2" R.B. FD.
173	RD-38	830,877.259	528,234.275	1,221.440	B.C. 1/4 COR.
174	HC-47	830,864.006	527,498.050	1,220.260	C,P.S. FD.
176	TP-76	828,228.333	528,223.153		1/2" R.B. SEC. COR.
178	HC-49	828,249.255	532,787.803	1,235.155	C.P.S. FD.
179		828,251.704	533,511.359		STONE SEC. COR.
181	TP-79	822,976.345	533,496.575		B.C. SEC. COR.
182	HC-54	822,950.510	530,856.782	1,231.545	1" P. 1/4 COR.
183	HC-53	822,929.745	528,202.563	1,224.805	1" P. SEC. COR.
185	HC-52	822,894.861	524,216.212	1,218.760	C.P.S. FD.
187	RD-39	828,191.361	524,295.271	1,218.445	C.P.S. FD.
189	HC-46	830,832.700	524,315.796	1,219.920	C.P.S. FD.
192	RD-36	836,252.737	524,325.111	1,216.785	C.P.S. FD.
194	HC-35	838,895.979	524,329.512	1,215.510	C.P.S. FD.
195	HC-36	838,882.599	526,857.095	1,219.990	B.C. FD.
199	RD-28	844,169.873	524,338.642	1,217.890	C.P.S. FD.
210	HC-31	846,843.095	554,605.752	1,273.940	C.P.S. FD.
211	RD-31	844,149.384	554,588.316	1,279.175	B.C. SEC. COR.
213	RD-30	844,150.841	550,421.950	1,269.755	C.P.S. FD.
214		844,168.767	549,313.015		B.C. SEC. COR
217	HC-39	838,898.554	546,641.175	1,265.870	1/2" R.B.
218	HC-40	838,898.561	549,279.515	1,269.850	B.C. SEC. COR.
219	RD-32	837,395.027	549,270.726	1,271.465	C.P.S. FD.
221	RD-37	833,608.738	549,247.680	1,276.300	B.C. SEC. COR.
222	HC-45	833,595.259	546,652.885	1,268.270	C.P.S. FD. 1/4 COR.
224	HC-44	833,590.089	543,951.611	1,266.945	P.K. FD.
225		833,590.152	543,994.021		1" P. SEC. COR.
226	VC-23	830,975.038	543,972.517	1,264.625	C.P.S. FD.
227	RD-40	828,341.326	543,954.571	1,262.815	B.C. SEC. COR.
228	RD-50	828,322.086	543,337.482	1,262.950	C.P.S. FD.
229	HC-51	828,320.804	546,043.898	1,269.255	C.P.S. FD.
230	VC-26	825,696.084	543,945.383	1,264.155	1" P. FD.
231	HC-56	823,043.928	543,290.524	1,264.615	C.P.S. FD.
232		823,050.314	543,936.212		B.C. SEC. COR.
233	RD-41	823,033.033	541,277.195	1,259.060	1" P. 1/4 COR.
234	HC-55	823,022.156	540,053.853	1,254.110	C.P.S. FD.
235	TP-96	823,016.885	538,774.123		BAR & CAP SEC. COR.
246	TP-98	849,419.577	559,834.010		B.C. SEC. COR.
248	HC-34	844,151.975	559,825.024	1,290.200	B.C. SEC. COR.
250	TP-101	844,157.937	565,059.645		1/2" R.B. FD. SEC. COR.
252	RD-34	838,902.143	565,083.954	1,308.705	B.C. SEC. COR.
254	HC-42	837,069.183	568,569.310	1,320.090	1/2" R.B. FD.
255	RD-35	836,282.105	568,203.094	1,318.580	1/2" R.B. FD.
256	HC-43	834,391.797	567,169.030	1,322.840	C.P.S. FD.
260	RD-33	838,890.637	561,181.924	1,300.460	RR. SPK. FD.
261	TP-106	838,887.220	559,815.917		B.C. SEC. COR.
262	HC-41	840,217.041	559,830.527	1,295.815	C.P.S. FD.
265	HC-33	844,683.239	553,635.421	1,273.940	1/2" R.B. FD.
268	HC-30	846,420.140	551,740.650	1,267.830	1/2" R.B. FD.
271	RD-27	847,825.049	549,334.481	1,264.255	C.P.S. FD.
276	HC-59	817,644.227	529,514.897	1,232.255	C.P.S. FD.
277	HC-58	817,617.435	526,505.716	1,227.690	LEAD & TACK FD.
278	RD-42	817,631.872	528,179.644	1,228.545	1/2" R.B. FD.
280	RD-45	812,342.461	528,158.065	1,225.033	B.C. SEC. COR.
282	HC-64	807,052.815	528,136.456	1,227.905	B.C. SEC. COR.
283	HC-63	807,046.109	525,788.556	1,219.760	C.P.S. FD.
285	HC-68	801,723.722	525,438.671	1,219.275	
286	HC-67	801,726.409	522,818.548	1,214.680	B.C. SEC. COR.
288	TP-120	807,018.242	522,841.643		B.C. SEC. COR.
289	HC-62	807,030.161	523,988.976	1,216.005	P.K. FD.
291	RD-44	812,311.250	524,269.412	1,218.180	N.& S. FD.
293	HC-57	817,608.163	524,163.872	1,221.250	C.P.S. FD.
301	RD-43	817,725.506	539,361.961	1,258.160	C.P.S. FD.
302	TP-125	817,717.561	538,751.229		B.C. SEC. COR.
304	HC-61	812,406.823	539,874.706	1,260.190	C.P.S. FD.
305	RD-47	812,419.811	538,729.013	1,256.810	B.C. SEC. COR.
306	RD-46	812,415.390	537,398.830	1,253.850	C.P.S. FD.
307	HC-60	812,411.099	536,100.381	1,248.600	B.C. 1/4 COR.
309	HC-65	807,119.988	536,739.144	1,247.785	C.P.S. FD.
310	HC-66	807,126.939	539,833.917	1,253.340	C.P.S. FD.
311	RD-48	807,136.313	538,780.725	1,251.825	1" L.P. FD.
313	TP-129	807,109.716	533,440.218		B.C. SEC. COR.

LEGEND
- ▲ HC - HORIZONTAL CONTROL
- ■ RO - READ ONLY
- ▲ SECTION CORNNER

GILBERT-CHANDLER BENCH MARKS
FRANZOY-COREY ENG.
STUDY 1989

CENTRAL FILES
314
DRAWER #

GILBERT-CHANDLER BENCH MKS
1989- FRANZOY COREY

Franzoy·Corey
ENGINEERS & ARCHITECTS
Corporate Headquarters • 7776 Pointe Parkway West
Suite 290 • Phoenix, Arizona 85044 • (602) 438-2200
